

Practical

Follow the assignment guidelines under the appendix.

Practical 1

1. Analyse the background of your selected software project.
 - Describe the project development team (the project development team is your group).
 - Describe who your project client is, the nature of their business, and explain why the client wants to carry out the project.
2. Perform project initialisation activities
 - Project costs estimation (This may include hardware, software, manpower, etc).
 - Identify one objective of this project (must conform to the SMART criteria)
 - Project team structure
 - Stakeholders register
 - Communication plan
 - Project scope: create a work breakdown structure (WBS) which shows 3 levels: system, modules, and functions. Briefly describe the functionalities of each module.
 - Exclusions

Practical 2**Project Planning**

This is focused on the activities in project planning and estimation, which include defining activities, sequencing activities, estimating resources, estimating durations, and developing the project schedule.

1. Identify one suitable software process model used (apply stages of selected model to a Gantt chart) and the required tasks for this project.
2. Prepare a project schedule using **Microsoft Project software**,
 - Enter the project information with the appropriate start and/or finish date.
 - Set the base calendar for the project with the appropriate workdays, working hours or include exceptions such as public holidays, etc.
 - Prepare a Gantt chart (*Microsoft Project software*) with the task name, duration, and task dependencies. Allocate staff (resources) to project tasks.
 - Tasks and subtasks must include the estimated durations, concurrency, and task dependencies (predecessor) information.
 - Adjust the time scale, deadlines, and set milestones.

<See Figures 1 and 2 for samples>

Practical 3**Resource Management**

1. Determine the **resources** (e.g., staff, equipment, materials, expenses, etc.) required for the various tasks or subtasks. Estimate the staff costs in the project schedule.
2. Assume that you have acquired your project team (members' skills and responsibilities), and allocate each team member to the project's tasks or subtasks.
3. Describe any 2 **assumptions** you made while creating the project schedule.
4. Resource scheduling depends on the project calendar, task dependencies (predecessor), and manpower. If there is any *resource overallocation*, apply *resource leveling* in the Gantt chart and revise your project schedule accordingly.
5. Generate **two reports** using Microsoft Project software

<See Figure 3 for samples>

Practical 4

1. Identify one important **software quality attribute** for the system. For the quality attribute, specify the **quality assessment process**.

Prepare a quality plan include the following details:

- Quality name: software quality attribute
- Description: description of the quality attribute

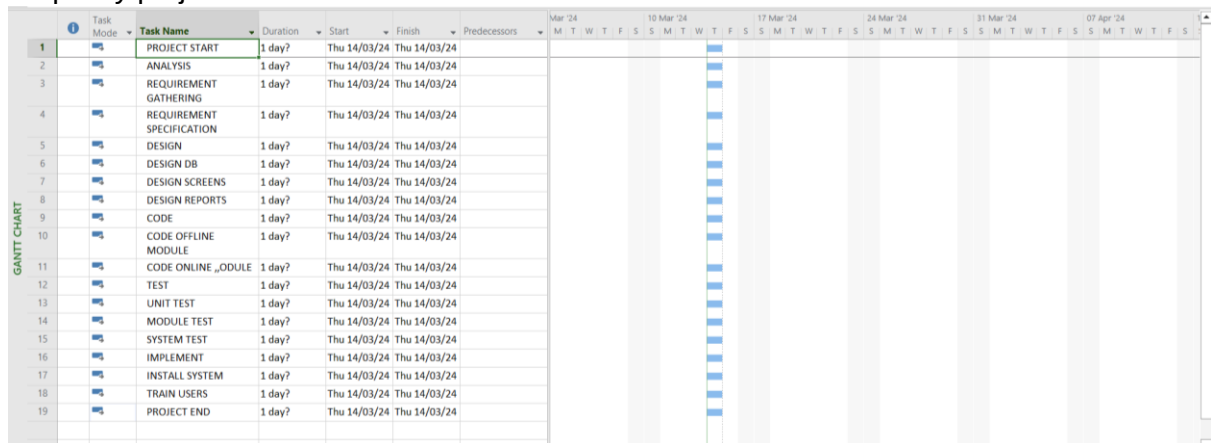
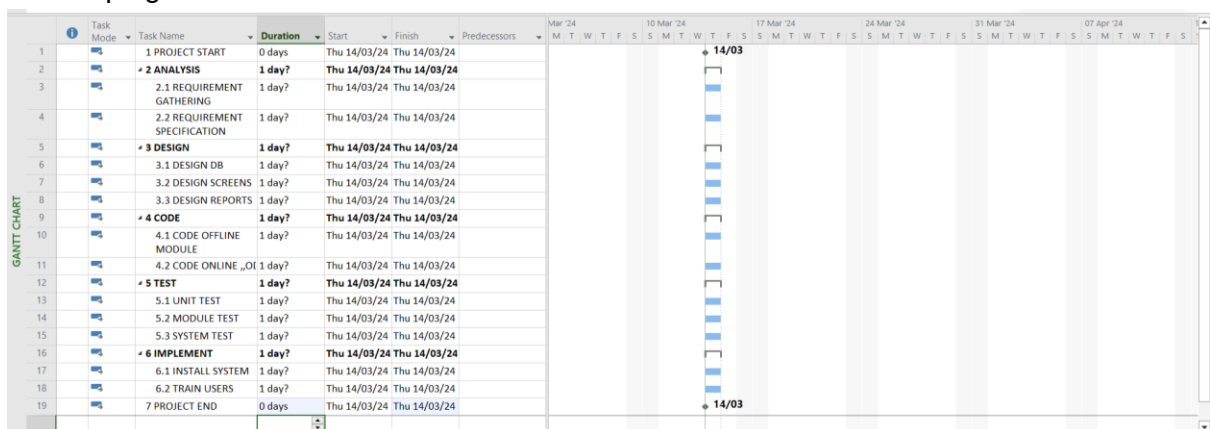
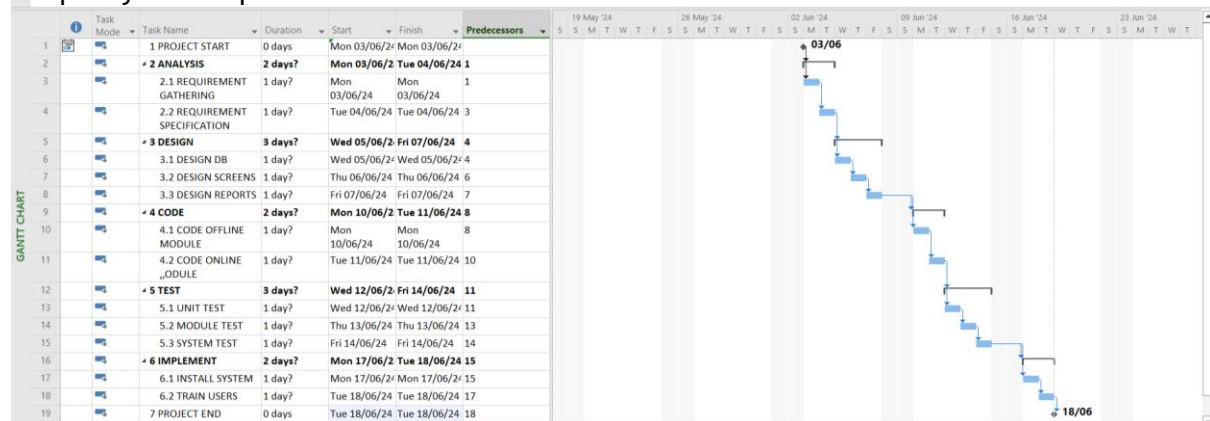
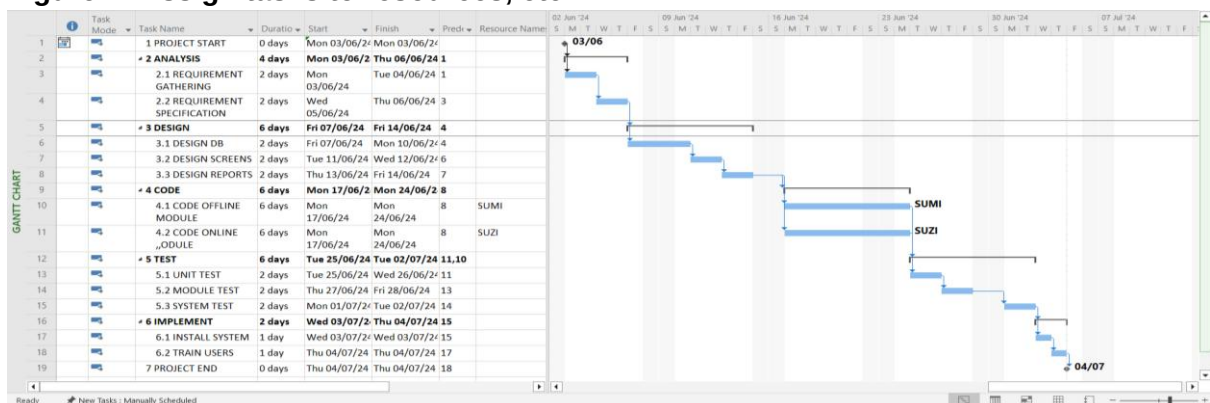
- Scale: unit of Measurement for the quality attribute
- Test: practical test of the extent to which the quality attribute exists in the system.
Identify the quality assessment process
- Acceptable: minimum value which might be acceptable if other characteristics compensated for it, and below which the system would have to be rejected
- The range of values within which the quality measurement value is expected to fall.
- Now: value applies currently.

Practical 5

1. Prepare Risk table (e.g. Risk information sheet in Chapter 5)
 - Identify 1 potential **risk** in your project. Briefly describe the risk and estimate its probability and impact. Lastly, your risk mitigation, monitoring, and management plans
2. Ethics and professional conduct for project management
 - Based on the Stakeholder Register, describe two appropriate strategies for **engaging key stakeholders** (specifically, the most influential/powerful stakeholder *and* potential end-users of the system)
 - Referring to the selected software process model, explain why it is also important to **disclose the disadvantages** of the chosen model to relevant stakeholders.
 - If your project is significantly behind schedule, propose two **corrective actions** to bring the project back on track. For each action, evaluate two advantages and two disadvantages.

Practical 6

1. Each team: prepare the presentation slides content for all assignment tasks.
2. Presentation marks given to each member..

Figure 1**1. Specify project tasks****2. Grouping tasks****3. Specify task dependencies****Figure 2: Assign tasks to resources, etc**

COST OVERVIEW

A bar chart with two horizontal bars. The top bar is blue and labeled 'COST' with a value of 'RM 91,960.00'. The bottom bar is orange and labeled '% COMPLETE' with a value of '59%'. The orange bar is shorter than the blue bar, indicating that 59% of the total cost has been completed.


Category	Value
COST	RM 91,960.00
% COMPLETE	59%

COST OVERVIEW


COST STATUS
Cost status for top level tasks.

Name	Actual Cost	Remaining Cost	Baseline Cost	Cost	Cost Variance
Planning	RM 12,640.00	RM 4,000.00	RM 0.00	RM 16,640.00	RM 16,640.00
Analysis	RM 8,960.00	RM 0.00	RM 0.00	RM 8,960.00	RM 8,960.00
Design	RM 8,000.00	RM 0.00	RM 0.00	RM 8,000.00	RM 8,000.00
Code Development	RM 5,330.00	RM 12,810.00	RM 0.00	RM 18,140.00	RM 18,140.00
Testing	RM 0.00	RM 14,940.00	RM 0.00	RM 14,940.00	RM 14,940.00
Deployment	RM 0.00	RM 25,280.00	RM 0.00	RM 25,280.00	RM 25,280.00

Progress made versus the cost spent over time. If % Complete line below the cumulative cost line, your project may be over budget.

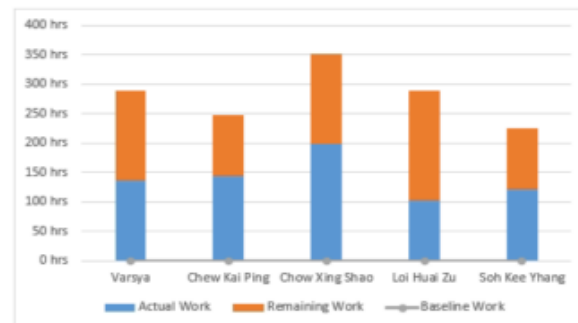


Cost status for all top-level tasks. Is your baseline zero?

[Try setting as baseline](#)

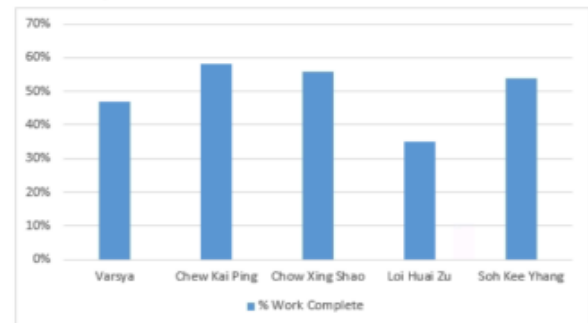
RESOURCE OVERVIEW

RESOURCE STATS
Work status for all work resources.



RESOURCE OVERVIEW

WORK STATUS
% work done by all the work resources



RESOURCE STATUS
Remaining work for all work resources

Name	Start	Finish	Remaining Work
Varsya	February 10, 2025	June 10, 2025	152 hrs
Chew Kai Ping	February 13, 2025	June 05, 2025	104 hrs
Chow Xing Shao	February 18, 2025	May 30, 2025	154 hrs
Loi Huai Zu	February 18, 2025	June 05, 2025	186 hrs
Soh Kee Yhang	February 21, 2025	June 05, 2025	104 hrs
